


**POLK COUNTY UTILITIES
COMMUNITY INVESTMENT PROGRAM
Quarterly One Page Report
Heritage Place Wastewater Gravity Main Improvements**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 2	Central	Wastewater Collection System Projects	2015-5-10-0	6841022

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

Scope:	Lining of approximately 4,000 linear feet of wastewater gravity main, sealing of 13 lateral connections, and coating of 6 manholes to mitigate groundwater infiltration to the waste water collection system.
Status:	As of December 31, 2016, construction has started with a substantial completion date of April 25, 2017.
Issues:	No issues at this time.

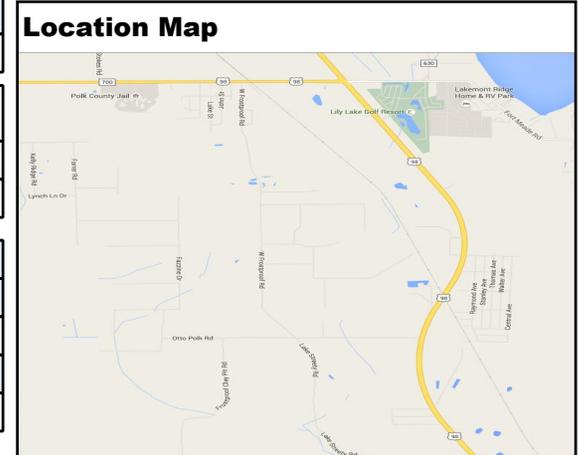

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$300,000.00		\$0.00	
Land/ROW	Design	Permitting	Construction
100.00%	100.00%	0.00%	5.00%

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design	4/30/2016																
Bid	08/10/2016																
NTP	11/09/2016																
Construction	4/30/2017																



Updated: 12/14/2016 9:29:58 AM
