


**POLK COUNTY UTILITIES  
COMMUNITY INVESTMENT PROGRAM  
Quarterly One Page Report  
540A 12" WM Extension to Old Hwy 37**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 2	Southwest	Water Distribution System Projects	2013-1-40-0	6834024

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

<b>Scope:</b>	The project consists of approximately 1,000 LF of 10" WM from Old Highway 37 to South Florida Avenue (SR 37). The new water main will provide a redundant connection between the east and west side of the water distribution system, thereby increasing system reliability.
<b>Status:</b>	The design is 90 percent complete. The project has received permits from Polk County ROW, DOH, and FDOT. The CSX permit is pending.
<b>Issues:</b>	No issues at this time.

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$315,000.00		\$985.02	
Land/ROW	Design	Permitting	Construction
100.00%	90.00%	75.00%	0.00%

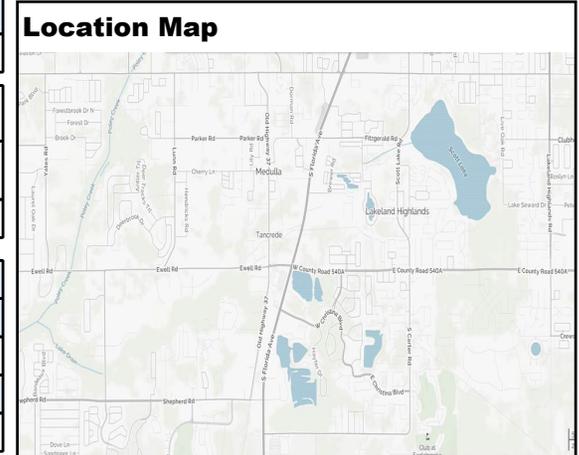

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design																	
Bid																	
NTP																	
Construction	5/20/2017																



Updated: 12/15/2016 1:31:32 PM
