

**POLK COUNTY UTILITIES  
COMMUNITY INVESTMENT PROGRAM  
Quarterly One Page Report  
US17/92 Reclaimed Water Main Improvements**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 4	Northeast	Reclaimed Water Projects	2017-2-20-0	6802029

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235


<b>Scope:</b>	Install 5,200 LF of 12-inch PVC RWM on US 17/92 from CR 54 south to Providence Blvd. Install 6,200 LF of 16-inch PVC RWM on US 17/92 from Providence Blvd. south to Sunny Acres Rd.
<b>Status:</b>	CSA 14 004 02 negotiated with Jones Edmunds. BoCC approved the CSA on 10/04/16 and a design NTP was issued 10/11/16. Final design expected 7/7/17. Construction projected to begin 10/7/17 and to be completed on 3/5/18.
<b>Issues:</b>	None at this time.

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$1,695,000.00		\$0.00	
Land/ROW	Design	Permitting	Construction
100.00%	5.00%	0.00%	0.00%


Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired	6/27/2011																
Design	7/7/2017																
Bid	9/5/2017									X							
NTP	10/7/2017									X							
Construction	6/6/2018																

<b>Notes:</b>	No easements anticipated at this time.
---------------	----------------------------------------

Location Map

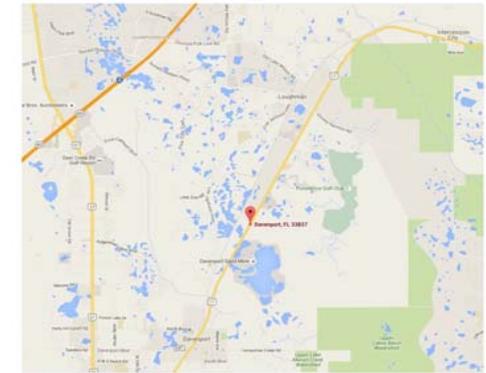

Project Image

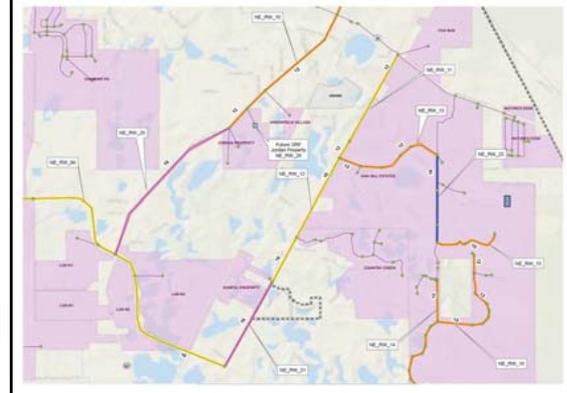

Updated: 12/14/2016 7:52:54 AM
