


**POLK COUNTY UTILITIES
COMMUNITY INVESTMENT PROGRAM
Quarterly One Page Report
Waverly Water System Treatment Evaluation**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 2	East	Water Treatment and Storage Facility Projects	2017-1-50-0	6815002

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

Scope:	Engineering study to evaluate long-term options for meeting Stage 2 Disinfection Byproduct Rule.
Status:	CPO 14 006 D for an engineering study with Tetra Tech has been developed. Evaluation NTP issued 10/31/2016 and kickoff meeting conducted 10/31/2016. Study summarizing system data, desktop evaluation findings, and recommendations anticipated 1/31/2017.
Issues:	None at this time.

Location Map

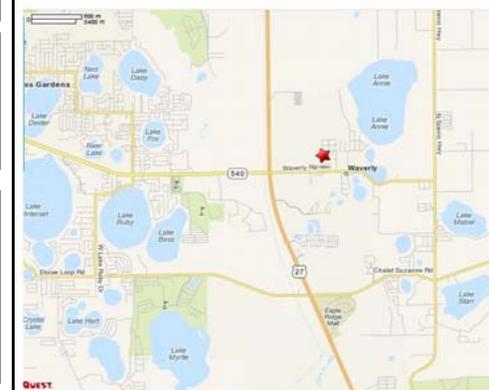

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$105,000.00		\$0.00	
Land/ROW	Design	Permitting	Construction
100.00%	0.00%	0.00%	0.00%

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design	1/31/2017																
Bid																	
NTP																	
Construction																	

Project Image



Updated: 12/14/2016 7:15:45 AM
