


**POLK COUNTY UTILITIES
COMMUNITY INVESTMENT PROGRAM
Quarterly One Page Report
Booster/Valve Station SCADA Upgrades**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	All Districts	Miscellaneous	Water Distribution System Projects	2016-6-70-0	6837013

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

Scope:	Upgrade existing valve and booster stations with local control capabilities and remote communications to allow for central monitoring and control of these systems. Provision of pressure reducing valve (PRV) monitoring to aid in distribution pressure control and notification of system pressure issues. Addition of controllers and communications will be provided for valve stations to monitor system flows and pressures and control valves and communications will be provided at existing booster stations to relay control and monitoring information that is currently only available locally at the facility.
Status:	As of December 31, 2016, the Carter Road reclaim booster station control system upgrades have been completed. PRV and system pressure logging instruments have been added to the Hallam Preserve potable water service area to monitor and report pressure data on a daily basis.
Issues:	No issues at this time.

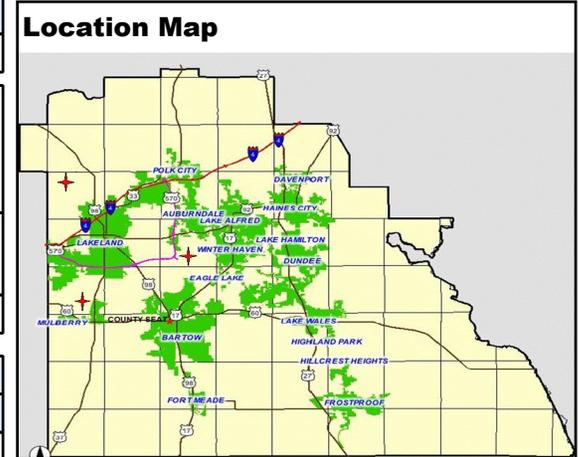

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$150,000.00		\$39,341.44	
Land/ROW	Design	Permitting	Construction
100.00%	100.00%	100.00%	25.00%

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design																	
Bid																	
NTP																	
Construction	9/30/2019																

Updated: 12/13/2016 4:44:02 PM
