


**POLK COUNTY UTILITIES  
COMMUNITY INVESTMENT PROGRAM  
Quarterly One Page Report  
FDC Grove Road Reclaimed Water Main Improvements**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 4	Northeast	Reclaimed Water Projects	2017-4-20-0	6802030

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

<b>Scope:</b>	Install 400 LF of 8-inch PVC RWM on Minute Maid Ramp Rd. 2 from existing RWM to Natures Reserve; install 8,100 LF of 8-inch PVC RWM on FDC Grove Rd. from Minute Maid Ramp Rd. 2 south to Sandhill Rd.; install 2,700 LF of 8-inch PVC RWM on Sandhill Rd. from US 27 to FDC Grove Rd.
<b>Status:</b>	CSA 14 007 02 negotiated with AMEC. BoCC approval 10/04/16 and design NTP issued 10/11/16. Final design expected 10/7/17. Construction projected to begin 5/7/18 and completed 12/28/18.
<b>Issues:</b>	Easement acquisition anticipated on FDC Grove Rd.

Location Map

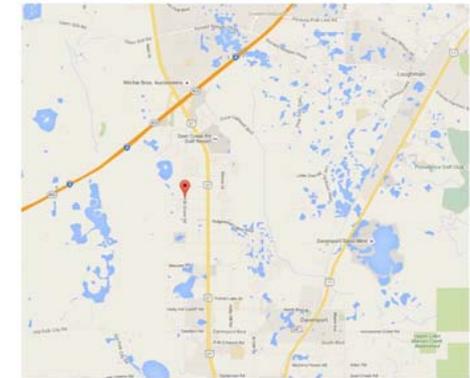

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$952,500.00		\$7,418.65	
Land/ROW	Design	Permitting	Construction
0.00%	0.00%	0.00%	0.00%

Project Image



Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired	3/17/2018																
Design	10/7/2017																
Bid	4/27/2018																
NTP	5/7/2018																
Construction	12/28/2018																

Updated: 12/14/2016 7:35:49 AM
