


**POLK COUNTY UTILITIES
COMMUNITY INVESTMENT PROGRAM
Quarterly One Page Report
US27 from US98 to Harvard Ave Potable Water Utility Relocations**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 2	Southeast	Water Distribution System Projects	2017-1-60-0	6834033

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

Scope:	Relocation of up to 20,000 linear feet of existing potable water distribution and transmission mains 10 to 12 inches in diameter as required to accommodate the widening of US Hwy 27 from CR 630A to Highlands County Line.
Status:	As of December 31, 2016, design is on hold due to delay of proposed road improvements.
Issues:	No issues at this time.

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$2,750,000.00		\$2,129.40	
Land/ROW	Design	Permitting	Construction
0.00%	0.00%	0.00%	0.00%

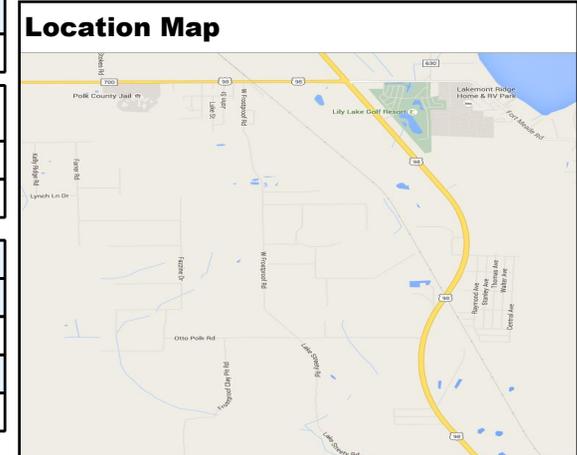

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design	9/27/2019																
Bid																	
NTP																	
Construction	9/30/2024																



Updated: 12/8/2016 9:06:29 AM

2014. 8. 4. 12:58
