


**POLK COUNTY UTILITIES
COMMUNITY INVESTMENT PROGRAM
Quarterly One Page Report
US27 from US98 to Harvard Ave Wastewater Utility Relocations**

Period Ending	Department	Commission District	Service Area	Project Type	PCU Project No	Oracle No
12/31/2016	Utilities	District 2	Southeast	Wastewater Collection System Projects	2017-2-60-0	6844016

Contacts	Name	Organization	Phone
Utilities Director	Marjorie Craig	Polk County Utilities	863-298-4235

Scope:	Relocation of up to 28,500 linear feet of existing wastewater collection and transmission mains 6 to 10 inches in diameter as required to accommodate the widening of US Hwy 27 from CR 630A to Highlands County Line.
Status:	As of December 31, 2016, design is on hold due to delay of proposed road improvements.
Issues:	No issues at this time.

PROJECT PROGRESS			
PROJECT BUDGET		EXPENDED TO DATE	
\$2,750,000.00		\$1,965.60	
Land/ROW	Design	Permitting	Construction
0.00%	0.00%	0.00%	0.00%

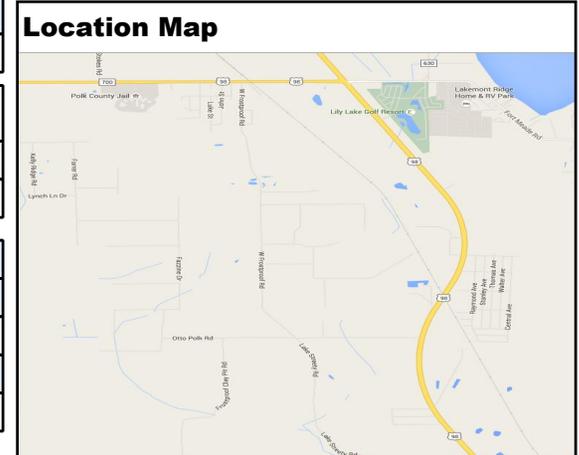

Phase/Contract	Completion	FY2015/2016				FY2016/2017				FY2017/2018				FY2018/2019			
		Q1	Q2	Q3	Q4												
Land Acquired																	
Design	9/27/2019																
Bid																	
NTP																	
Construction	9/30/2024																



Updated: 12/14/2016 10:05:15 AM
